




2025-26

IMPLEMENTATION STRATEGY

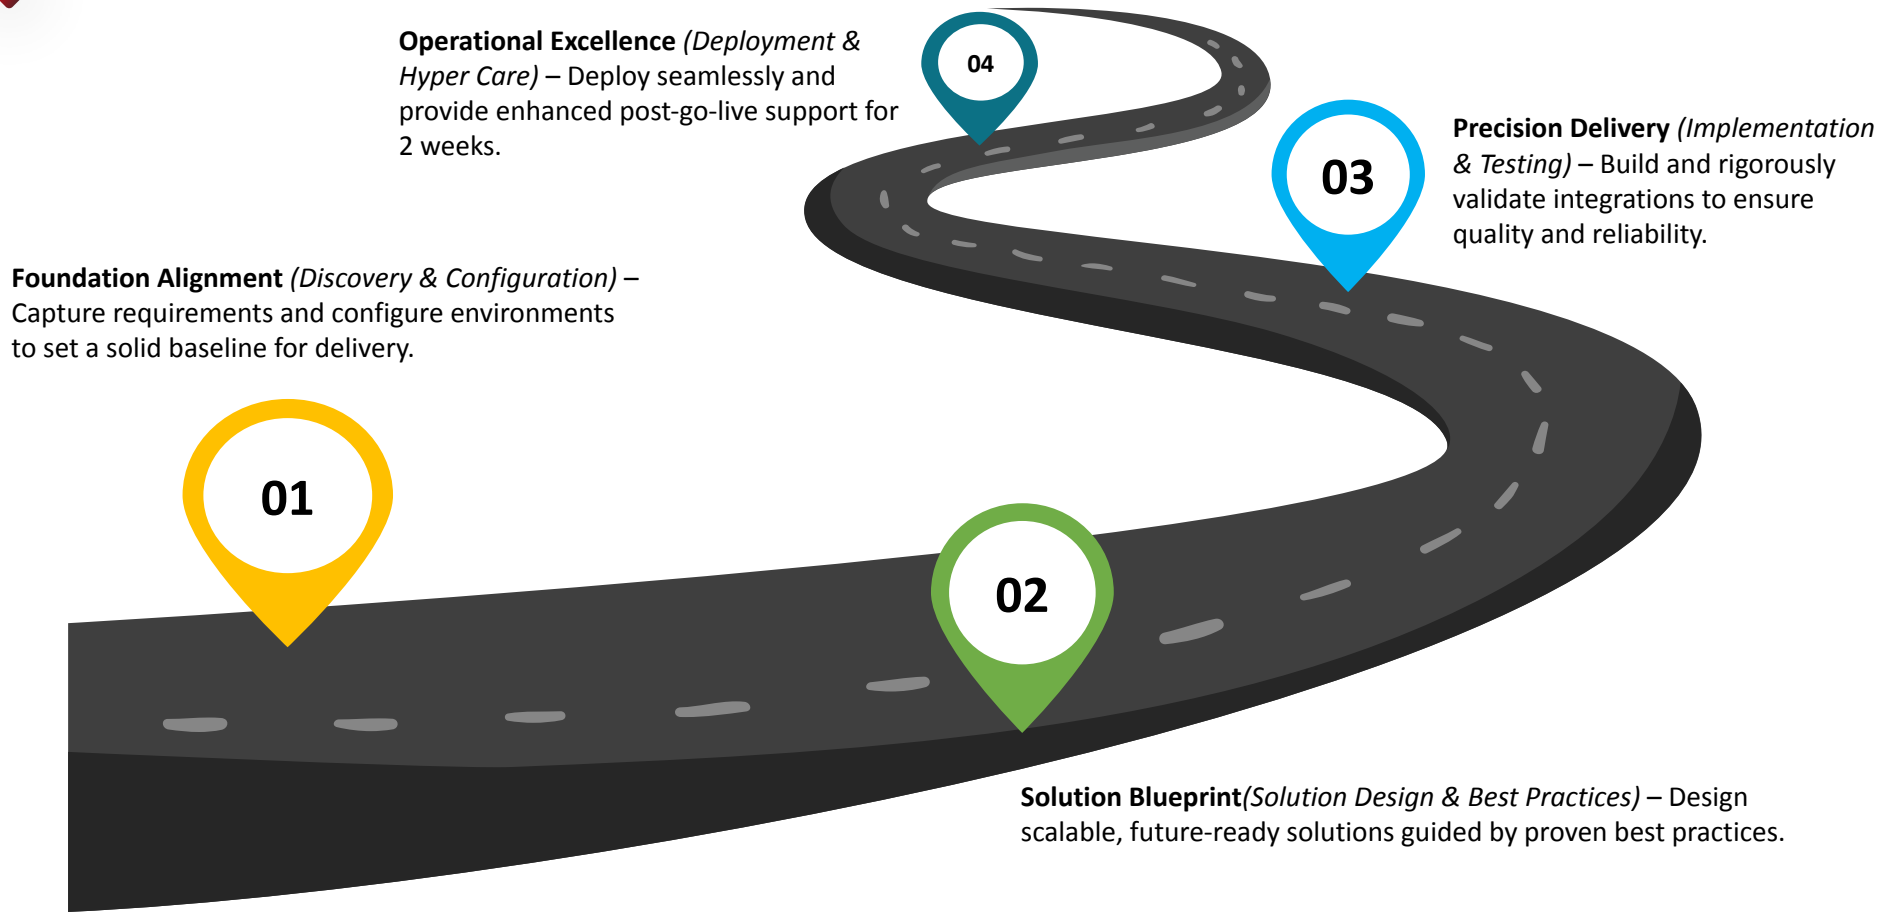

ROLE

PROJECT TEAM STRUCTURE



Solution Architect
Salesforce & Mulesoft




Project
Manager



Salesforce
Developers



MuleSoft
Developers

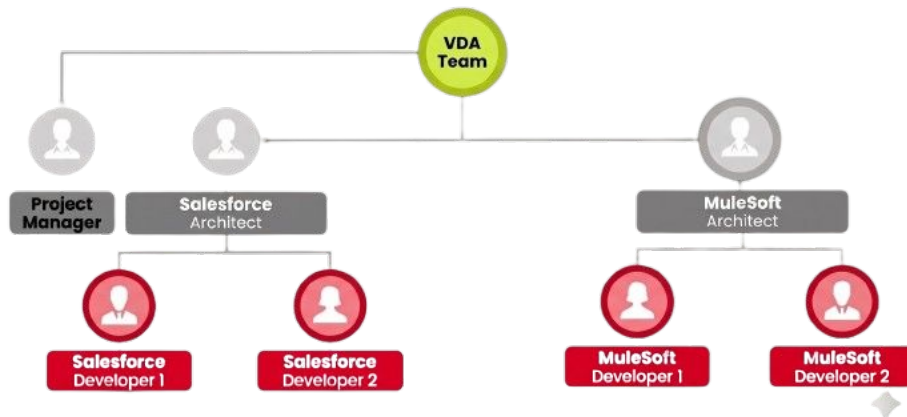

ESTIMATED TIME COMMITMENT*

High Level Service Cloud Implementation for VDA

WEEK	PHASE	VDA TEAM INVESTMENT	DATASKATE (PARTNER) EFFORT
1	Requirements	20%	80%
2	Design	20%	80%
3	Development	10%	90%
4-5	Development	5% - 10%	95% - 90%
6-9	Dev / Testing	5%	95%
10	Dev / UAT	30%	70%
11	Final UAT	75%	25%

*The implementation time was provided on the basis of the knowledge we have received before presenting this slide and can change based on the detailed scope of discovery

MILESTONE & TIMELINES*

Below is the proposed approximate milestone for salesforce implementation as per our knowledge

	MAY	JUNE	JULY	AUG
SOW & Onboarding	Signatures			
Requirement Gathering	1 Week			
Design & Develop	1 Week	8 Weeks		
System Integration Test			2 Weeks	
UAT & Deploy				1 Week

*Detailed Scoping Call would be required to provide exact estimates on timeline and price

MULESOFT IMPLEMENTATION SCOPE

Integration Name	Business Object	Source	Target	Requirement
Security Alert → Case Creation	Alert / Incident	CrowdStrike, SentinelOne, Sniper, Hunter	Salesforce (Case)	Ingest alerts from multiple security platforms and create cases in Salesforce with key details like severity, source, and summary
Case Update Sync → External Systems	Case / Incident Update	Salesforce	CrowdStrike, SentinelOne, Sniper, Hunter	Sync case updates (status, notes, resolution) from Salesforce back to originating systems to maintain consistency
Slack → Case Creation/Update	Message / Alert	Slack	Salesforce (Case)	Capture Slack messages and create cases in Salesforce with minimal field mapping
Case Notifications → Slack	Case Notification	Salesforce	Slack	Send notifications to Slack for case creation, status updates in Case

*Security Alert to Case Creation will be counted as individual flows for each Source System

ESTIMATED TIME COMMITMENT*

High Level Mulesoft Implementation for VDA

WEEK	PHASE	VDA TEAM INVESTMENT	DATASKATE (PARTNER) EFFORT
1	Requirements	20%	80%
2	Design	20%	80%
3	Development	10%	90%
4	Development	10%	90%
5	Development	5-10%	95-90%
6	Dev / Testing	5%	95%
7	Dev / Testing	5%	95%
8	Dev / UAT	25%	75%
9	Final UAT	75%	25%

*The implementation time was provided on the basis of the knowledge we have received before presenting this slide and can change based on the detailed scope of discovery

MILESTONE & TIMELINES*

Below is the proposed approximate milestone for MuleSoft implementation as per our knowledge

	AUG	SEPT	OCT	
Requirement Gathering	1 Week			
Design & Develop	1 Week	5 Weeks		
System Integration Test		3 Weeks		
UAT & Deploy			1 Week	

*Detailed Scoping Call would be required to provide exact estimates on timeline and price

ESTIMATED TIME COMMITMENT

Parallely Implementation of Service cloud + Mulesoft for VDA

	MAY	JUNE	JULY	AUG
SOW & Onboarding	Signatures			
Requirement Gathering	1 Week	1 Week		
Design & Develop	1 Week	8 Weeks		
		1 Week	5 Week	
System Integration Test			3 Weeks	
UAT & Deploy				1 Week

*Detailed Scoping Call would be required to provide exact estimates on timeline and price

IMPLEMENTATION INVESTMENT

Pricing and TimeLine Show Below are based on the knowledge we have received at high level . Final price will be determined based on the detailed scoping scheduled with the client

Project	TimeLine	Investment
Salesforce	11 weeks	20000 USD*
MuleSoft	9 weeks	15000 USD*



Proposed Next Step:
"Schedule Discovery call and
present SOW for signatures""



Call to Action: "Let's discuss how
we can accelerate your digital
transformation journey."



THANK -YOU



DataSkate

196 Princeton Hightstown Road,
Building 2A, Suite 11, West Windsor,
New Jersey 08550



<https://dataskate.io>

